



Bamberg County ORS Project

Monthly Status Report

3/1/22

Project Description


PRTC, through a grant from the South Carolina ORS Broadband Infrastructure Program, is constructing a buried all fiber network in southern Bamberg county. This project will provide much needed high speed broadband connectivity to the underserved rural residents in portions of Bamberg County. This project will begin in late September and Phase 1 should be complete by the mid March, 2022.

Phase 2 will be built between February and October of 2022. Residents can contact PRTC in early November to place their orders. Visit PRTC's website at www.prtc.us to learn more about our services and pricing.

Bamberg County ORS BIP Fiber to the Home

Phase 1

Phase 2

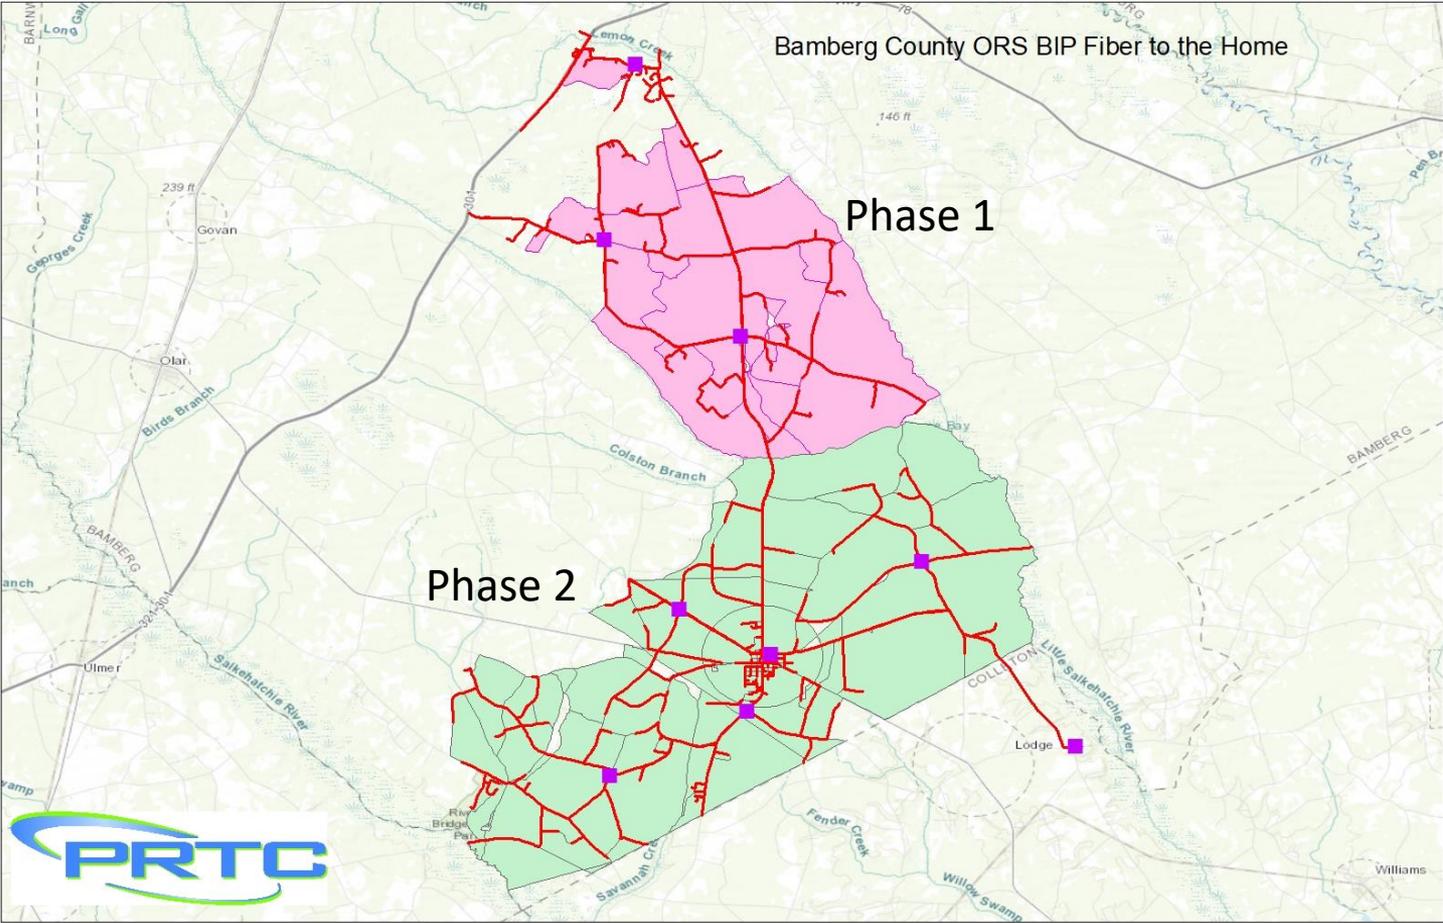

Project Timeline

	Design	Staking	Construction	Splicing/Testing	Installations
Phase 1	Complete	Complete	9/20 – 1/15	1/15 – 4/14	3/14 – 4/29
Phase 2	Complete	Pending	2/1/22 – 9/30/22	10/1 – 12/1	12/1 – 4/1/23

Detailed Timeline

Phase 1	Design	Staking	Construction	Splicing/Testing	Installations
Hadwin	Complete	Complete	Complete	1/1 – 2/14	3/14
Clearpond	Complete	Complete	Complete	2/15 – 3/14	4/4
Orange Grove	Complete	Complete	50%	3/15 – 4/14	4/14

Phase 2	Design	Staking	Construction	Splicing/Testing	Installations
Lodge	Complete	1/21	0%	5/1 – 6/1	6/1
Pocketville Rd	Complete	1/21	50%	6/1 – 7/1	7/1
Ashton Rd	Complete	Complete	0%	6/1 – 7/1	7/1
Rivers Brdg Rd	Complete	Complete	0%	9/1 – 10/1	10/1
Ehrhardt	Complete	3/25	0%	9/15 – 10/15	10/15

Zone	Miles of Fiber	Homes Passed	Status
Hadwin	9.6	103	Construction complete. Installations will begin 3/14.
Clearpond	32.58	187	Construction complete.
Orange Grove	10.4	151	Construction underway. 5.56 miles complete.
Lodge	22.73	80	
Pocketville Rd	20.64	106	Construction underway. 9.9 miles complete.
Ashton Rd	15.53	106	
Rivers Brdg Rd	21.21	66	
Ehrhardt	9.85	379	
Totals	142.54	1,178	

Thank You!
